

# HCRO site update




## Overview:

- Antennas
- Compute infrastructure
- Full buildout and developments
- Other updates



# Antennas:

- 1B e-stop problem solved
- Encoder problems:
  - 1J: no index
  - 5B: different index



Both encoders replaced

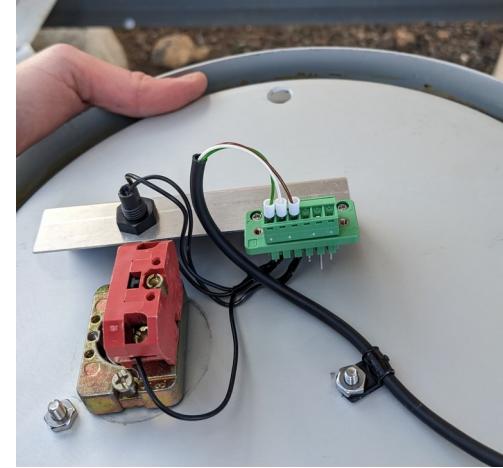

- 2E cryo cooler power cable replaced

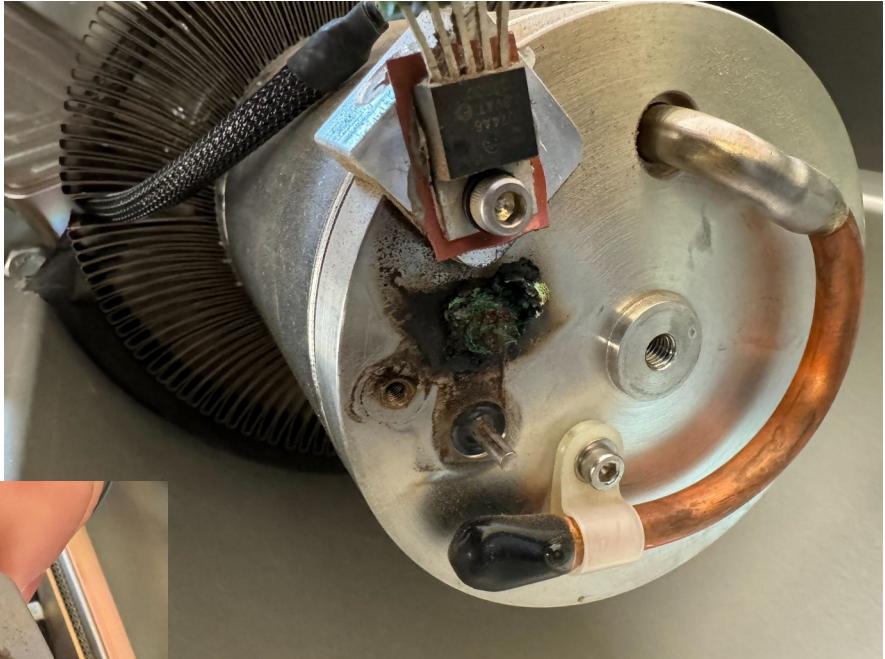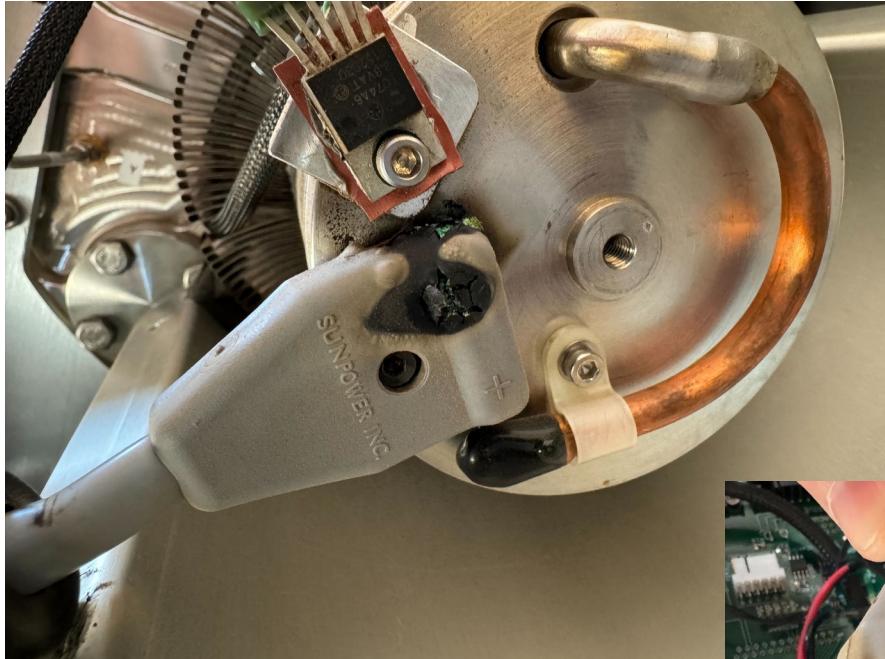

- Feed 20 sealed and vacuum started
- Will be soon ready for antenna 3C

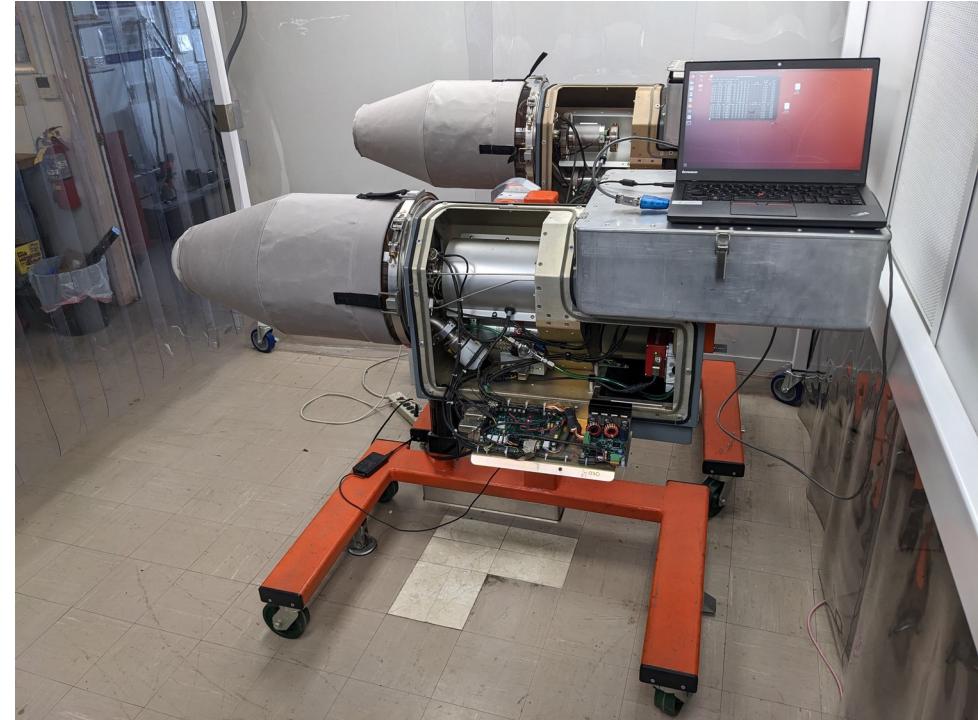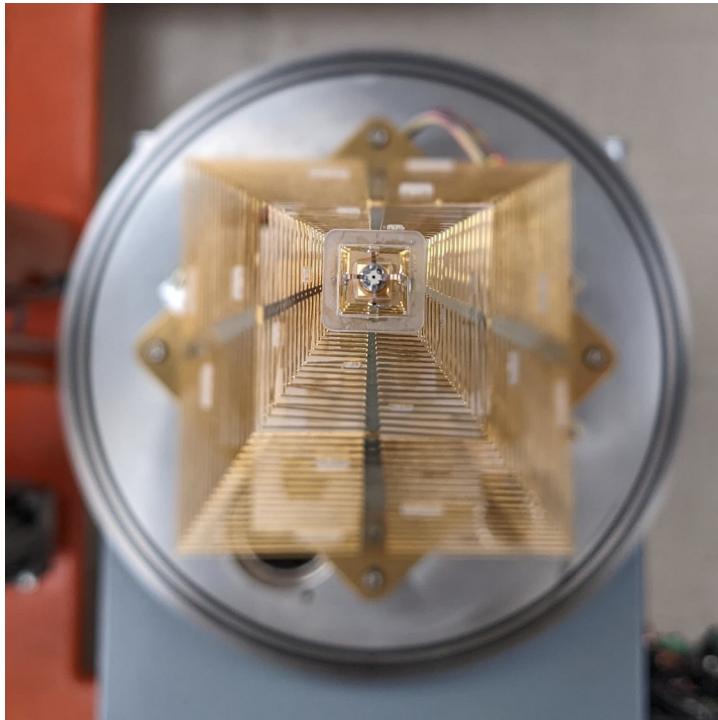


# Compute infrastructure:

- GlusterFS load balancing finished  
“zero size files” problem remains



# Full buildout and developments:

- Started IF-Splitter assembly and testing

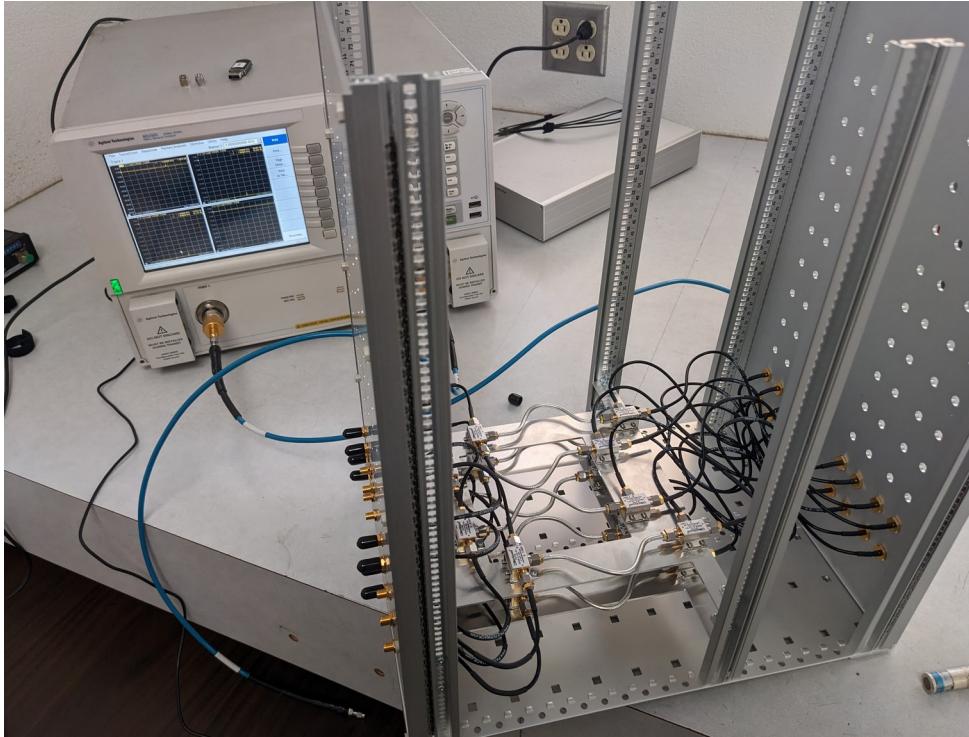

- Roy: Feed firmware
- Mike: PAX control box



# Other updates:

- NRDZ group on site
- Camera shelter cleanup

